

Growth Dashboard

Housing Roadmap Oversight Committee – September 2026

Allotments approved in the Greater Adelaide Planning Region

(Housing Roadmap 25 June 2024 to date)



Total allotments approved in South Australia since Housing Roadmap (25 June 2024 – 31 July 2026)


12,649

Total allotments approved in South Australia per financial year

Financial Year	Total Allotments
2020/21	3,723
2021/22	4,836
2022/23	5,289
2023/24	4,802
2024/25	6,604
2025/26	5,260
2026/27 (1 July to 31 August)	828

Total allotments approved in South Australia per month


(Housing Roadmap 25 June 2024 to date)

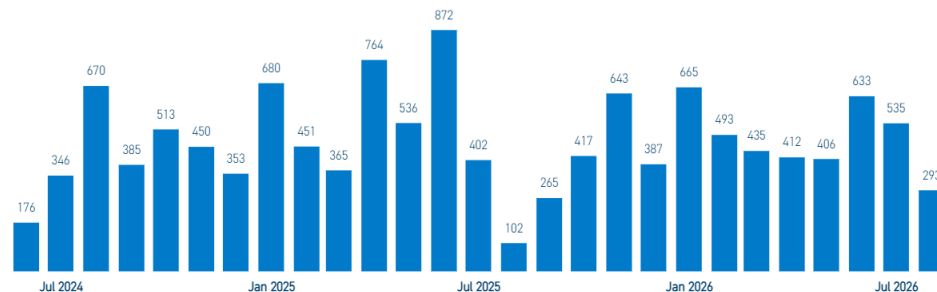

Metro Growth Program Delivery Summary (Housing Roadmap 2024)

Total Program pipe lay distance (as at 30 August 2026)	Life to Date (since 1 July 2024) 55,714 metres	FY 26/27 5,206 metres
Total current active crews (as at 30 August 2026)	32 crews: 12 open trench; 8 valves/tie-ins; 12 other works	

- More than 55 km of Metro Growth water and wastewater pipe laid.
- Program's expenditure forecast within total budget of \$1.192B.
- Asset in service achieved for 6 out of 20 districts all ahead of Housing Roadmap 2024 commitments

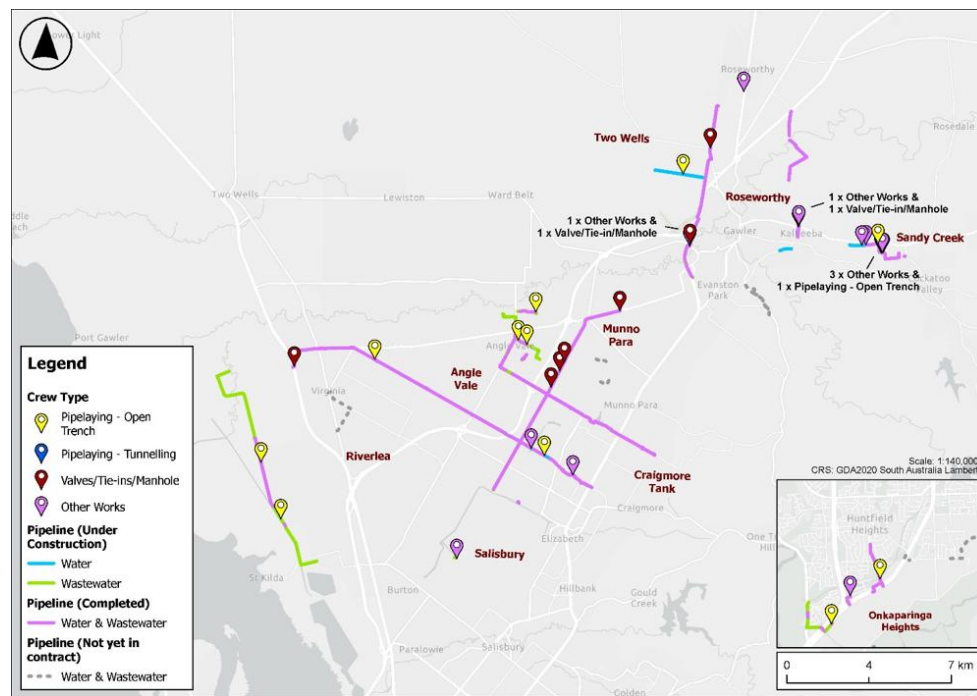

Active Metro Growth construction crew locations as at **30 August 2026**.

Delivery Schedule Angle Vale

Revised December 2025

	2024				2025				2026				2027				2028			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Angle Vale Water	Stage 1				Stage 1				Asset in Service											
Angle Vale Wastewater	Stage 2a				Stage 2a				Asset in Service											
					Stage 3				Stage 3											

Key drivers of delivery:	- System capacity - Developer expectations	Water works to be done:	DN1200 trunk main from the Craigmores tank; DN1000 trunk main Curtis Rd; DN750 main in Curtis Rd
		Wastewater works to be done:	Pump station upgrades including new pumps and electrical equipment 3.7 km sewer mains; 3 pump stations; 2.4 km DN300 pumping main
Delivered so far:	Water – Asset in service for inlet/outlet mains to/from Craigmores Tank (5,825m). Commissioning complete and asset in service for Heaslip Road water pipe (580m) Wastewater – Completed wastewater pump stations at Bunnings and Miravale. Pipelaying complete on Curtis Road (1,632m) and Curtis Road/Heaslip Road roundabout (397m). Commissioning complete and asset in service on Macon Road (357m).	New services capacity:	Water 1,400; Wastewater 800 (Stage 2a); and Wastewater 2,200 (Stage 3)

Overall Status



On track for delivery

Progress Comment

WATER Stage 1 (Tranche 1):

All assets in service.

WASTEWATER (Tranche 1):

Miravale pump station asset in service.

WASTEWATER STAGE 3 (Tranche 2):

Pipe laying on Fradd Road (Item 6) continuing: 51% or 407m of 803m pipe laid.

Pipe laying on Heaslip Road (Item 7) continuing: 82% or 1,347m of 1,649m pipe laid.

Pipe laying on Ashwin Street, Broster Road and Luis Drive (Item 11) continuing: 88% or 682m of 774m pipe laid.

Pipe laying on Rosetta Drive (Item 16) continuing: 70% or 87m of 124m pipe laid.



Government of
South Australia



Delivery Schedule Roseworthy

Revised December 2025

	2024				2025				2026				2027				2028			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Roseworthy Water	Stage 1				Stage 1															
Roseworthy Wastewater					Stage 2				Stage 2											

Overall Status



On track for delivery

Progress Comment

WATER STAGE 1 (Tranche 1):

Pressure Reducing Valve nearing completion pending developers connection for commissioning.

Gawler East Booster Pump Station mechanical works nearing completion and heating, ventilation and air conditioning works continuing.

WASTEWATER (Tranche 1):

Roseworthy Stage 1: Asset in service.

Roseworthy Stage 2:

Pipe laying on Gawler Bypass continuing: 93% or 2,565m of 2,749m pipe laid.

Manhole construction continuing on Gawler Bypass ready for bridge crossing works. Pump station electrical works nearing completion and two surge vessels installed.

Roseworthy

Key drivers of delivery:

- Services new homes
- System capacity
- Developer expectations

Water works to be done:

4 km DN750 trunk main duplication, Gawler East Pump Station; Roseworthy Booster Pump Station upsize, Sandy Creek DN1000 trunk main

Wastewater works to be done:

5.7 km of gravity sewer main, 2 km pumping sewer main, new pump station

Delivered so far:

Water – Asset in service for pipes on Martin Road, Sunnysdale Avenue and Kemp Road (3,962m).

Wastewater – Pipe laying complete on Twardz Road, Redbanks Road and Kentish Road (4,520m). Pipe laying complete on Paternoster Road (1,770m).

New services capacity:

Water 2,033
Wastewater 1,500




Government of
South Australia



Delivery Schedule Riverlea

Revised December 2025

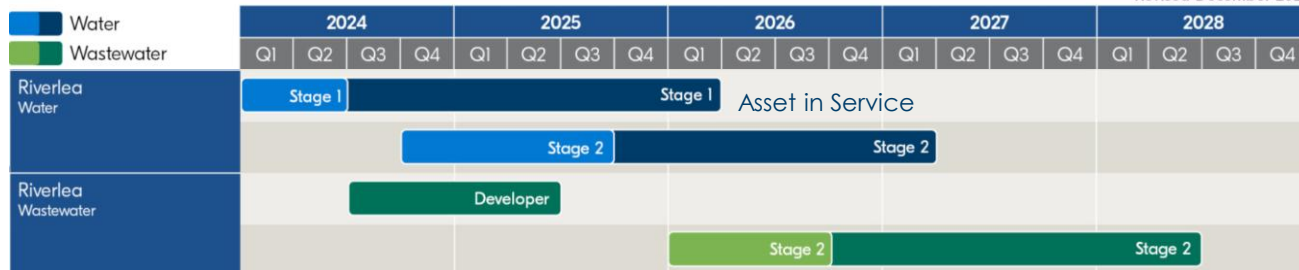

Overall Status



On track for delivery

Progress Comment

WATER STAGE 1 (Tranche 1):

Asset in service.

WATER STAGE 2 (Tranche 2):

Pipe laying on Robert Rod continuing: 99% or 7,440m of 7,500m pipe laid.

Pipe laying on Petherton Road continuing: 74% or 1,635m of 2,210m pipe laid.

Pressure reducing valve building precast walls installation commenced.

WASTEWATER STAGE 2 (Tranche 2):

Pipe laying on Brooks Road continuing: 70% or 2,895m of 4,163m pipe laid.

Riverlea

Key drivers of delivery:

- Services new homes
- System capacity
- Developer expectations

Water works to be done

Trunk Main duplication: 1.3 km DN1200; 3.4 km DN750; 7 km DN1000 trunk main; 3 km DN1200 trunk main, pressure reducing works, headworks connectors

Wastewater works to be done:

Arrangements agreed with developer for Stage 1 15 km sewer pumping main

Delivered so far:

Water: Stage 1: Asset in Service

Water: Stage 2: Pipe laying 99% complete on Robert Road and 74% complete on Petherton Road.

Wastewater: Pipe laying 70% complete on Brooks Road.

New services capacity:

Water 3,980
Wastewater 5,095



Government of
South Australia



SA Water

Delivery Schedule Virginia

Revised December 2025

	2024				2025				2026				2027				2028			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Virginia Water																				

Stage 1

Stage 1

Overall Status



On track for delivery

Progress Comment

WATER STAGE 1 (Tranche 2):

30% design and safety in designs complete. 60% designs underway.

Construction planned to commence Q1 2027 .

Virginia

Key drivers of delivery:

- Services new homes
- System capacity

Water works to be done

800 m DN450 water main; 450 m DN600 water main

Wastewater works to be done:

Nil

Delivered so far:

30% design and safety in designs complete

New services capacity:

Water: 700
Wastewater: none



Government of
South Australia



Delivery Schedule Gawler East

Water

Wastewater

Gawler East

Water

Revised December 2025

2024				2025				2026				2027				2028			
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4

Overall Status



On track for delivery

Progress Comment

WATER (Tranche 2):

Construction start has moved from Q2 2026 (inlet and outlet pipe) to a single construction period including both pipe and the booster pump station, which commenced late August 2026. This creates efficiencies through improved work sequencing and mobilisation cost savings.

Land access has been granted to SA Water by the developer. Site mobilisation and start up commenced on August 2026.

Gawler East (Springwood)

Key drivers of delivery	Developer expectations	Water works to be done	New Gawler East Pump Station
		Wastewater works to be done	Proposed delivery by Developer
Delivered so far	Site mobilisation and start up commenced for Gawler East booster pump station.	New services	Water: 1,600 Wastewater: by developer



Government of
South Australia



Delivery Schedule Two Wells

Revised December 2025

	2024				2025				2026				2027				2028			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Water																				
Wastewater																				
Two Wells Water																				

Overall Status



On track for delivery

Progress Comment

WATER (Tranche 2):

Pipe laying commenced on Parkers Road:
5% (134m) of 2,460m pipe laid.

Two Wells

Key drivers of delivery	- Services new homes - System capacity	Water works to be done	2.3 km DN750 water trunk main duplication
		Wastewater works to be done	None
Delivered so far	Pipe laying commenced on Parkers Road.	New services	Water: none Wastewater : none



Government of
South Australia



Delivery Schedule Onkaparinga Heights



Overall Status



On track for delivery

Progress Comment

WATER (Tranche 2):

Asset in Service.

WASTEWATER (Tranche 2):

Adel Circuit pipe laying complete.

Pipe laying on River Road continuing: 16% or 166m of 1,054m pipe laid.

Pipe laying on Brodie Road continuing: 29% or 41m of 143m pipe laid.

Hackham (Onkaparinga Heights)

Key drivers of delivery	Developer expectations	Water works to be done	1.3 km DN300 water main
		Wastewater works to be done	1.4 km of 150 mm to 300 mm sewer main
Delivered so far	Water – Asset in Service. Wastewater – Pipe laying complete on Adel Circuit (198m). Pipe laying 16% complete on River Road and 29% complete on Brodie Road.	New services	Water: 1,500 Wastewater: 1,600




Government of
South Australia



Delivery Schedule: connecting services

Revised December 2025

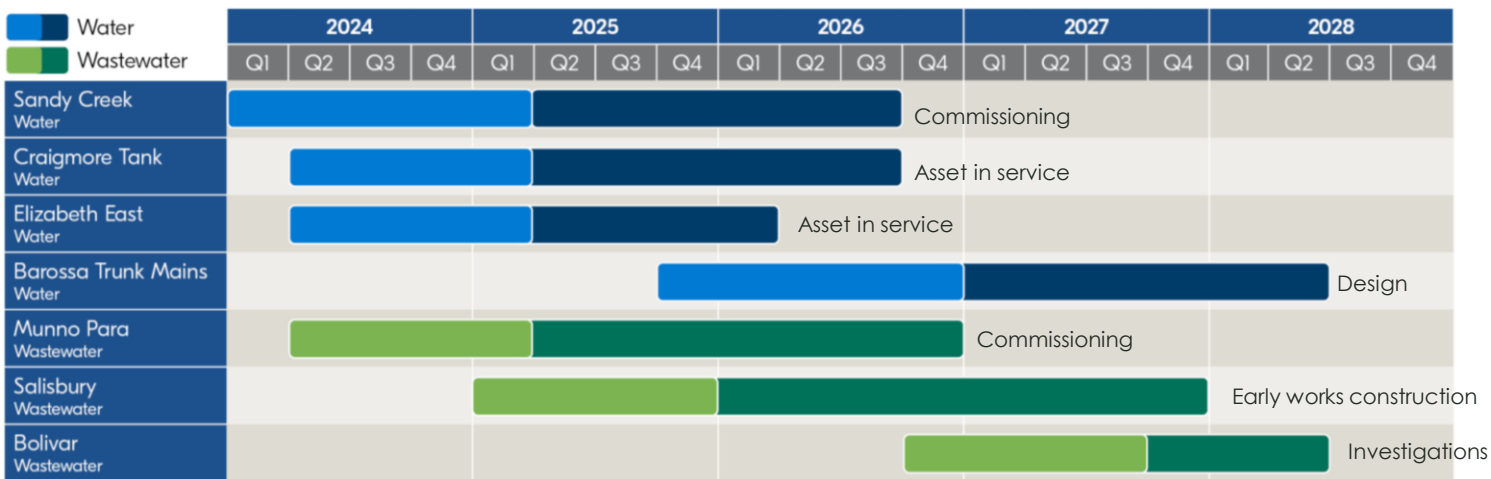

Design Construction

Connecting Water and Wastewater

Key drivers of delivery	System capacity
Water connecting works	Sandy Creek tank: inlet valves, control valves, facility upgrades, tanks, land acquisition Craigmores tank: inlet valves, control valves, facility upgrades Elizabeth East tank: inlet valves, control valves, facility upgrades Barossa Trunk Main: section upgrades
Wastewater connecting works	Munno Para: 10km trunk main, cross-connection Salisbury Capacity Upgrade: tank storage, odour control Bolivar WWTP: capacity



Government of
South Australia



making life flow



Government of
South Australia

